


**TOWN OF NAGS HEAD FY 18/19
PROJECT CONSTRUCTION UPDATE
April 3, 2019**

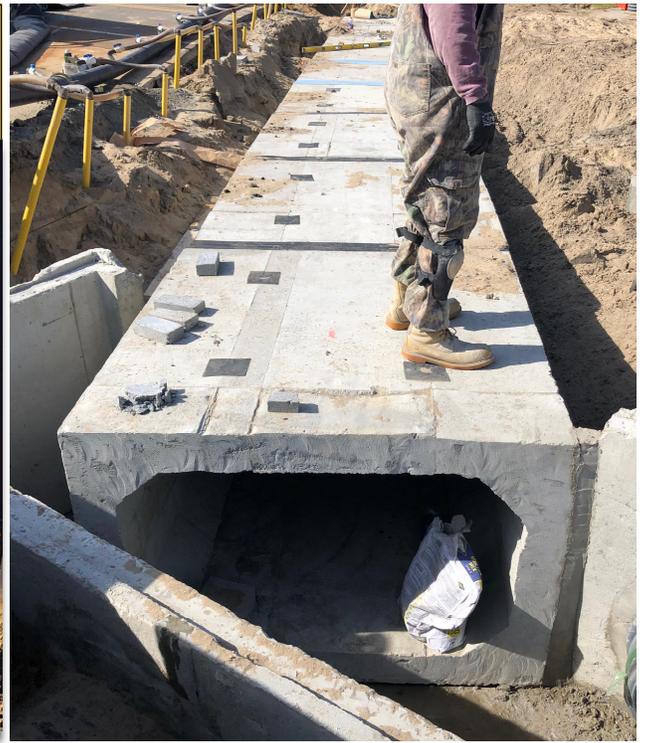

**PROJECT AREA #1
(UPSTREAM END OF RED DRUM OCEAN OUTFALL)**

WORK DESCRIPTION

Replacement of (2) 30" dia. cross street drainage pipes with 32" x 54" reinforced concrete box culvert with 18" dia. cross pipe, drop inlet structures, appurtenances and incidental work.

WORK PROGRESS

The construction work for the watermain was conducted Monday evening and completed mid-day on Tuesday. Water service has been restored in the area between Eighth St. and Baltic St. along the S. Virginia Dare Trail corridor. The Low Pressure Advisory that had been effect has been rescinded as of 3:00 pm on Wednesday March 27, 2019.

The contractor has commenced with the installation of the junction box vault and reinforced concrete box structure sections which span S. Virginia Dare Trail. The concrete box culvert installation is approximately 75% complete at this time. The completion of the box culvert installing is scheduled to occur over the course of the next week, weather permitting.

Sea Green Gallery, Surfin Spoon Frozen Yogurt Bar, Red Drum Grille & Taphouse remain open and residences along the work zone corridor will remain open to local traffic. Pedestrian access between Abelone St. and Gallery Row is restricted during construction. We ask our residents and visitors to exercise caution in the area around the construction work zone.

PROJECT SCHEDULE—

** Reference Project Area #1—Road Detour Overview for specific Temporary Road Closure Information*

BEGIN: In Progress

COMPLETE: Early May 2019

EXPECTED WORK CONDITIONS*

Temporary Road Closure between Abelone St. and Gallery Row, temporary traffic detour, temporary pedestrian closure and detour, local traffic access, trench excavation and bypass pump operation.

**CONTACT
INFORMATION**

Contractor | Hatchell Concrete Inc. | 252.473.6074 | hatchell_concrete@earthlink.net

Town of Nags Head | David Ryan, P.E. | 252.441.6221 | david.ryan@nagsheadnc.gov

